

***SPS BOND 2023
PROJECTS REPORT
02.10.2026***



HS PHASE 1 AND 2 – CONSTRUCTION PHASE

- Owner, Architect, and Constructor (DAC) meetings are scheduled for every two weeks to review construction progress and coordination with upcoming installations of SPS Owner provided equipment and systems.
- Areas 1, 2 and 3 are anticipated for 505 Architects and SPS to do a Punch in March 2026.
- SPS FF&E Procurement is underway with orders placed for all the previous approved bids and we are awaiting confirmation of delivery dates from each of the Vendors.

HS PHASE 1 AND 2 – CONSTRUCTION PHASE



JANUARY 5, 2025



FEBRUARY 2, 2026

HS PHASE 1 AND 2 – CONSTRUCTION PHASE

The following is a WORK SUMMARY of construction progress by Area:

SITE

Structural soil installation is complete

All structural paving installation is complete

All non-colored sidewalks installation is complete

Landscaping (trees/sod/irrigation) is in progress

AREA 1

Carpet flooring is in progress


Epoxy flooring installation is complete

MEP trim out is in progress

Ceiling tile installation is in progress

Final paint is in progress

Interior storefront is in progress



HS PHASE 1 AND 2 – CONSTRUCTION PHASE

WORK SUMMARY CONTINUED

AREA 2

Carpet flooring is in progress

Epoxy flooring installation is complete

Basketball goals and gym divider is installed

Toilet partition and accessory installation is in progress

Final paint is in progress


AREA 3

Carpet flooring is in progress

Epoxy flooring installation is complete

Toilet partition and accessory installation is in progress

Final paint is in progress



HS PHASE 1 AND 2 – CONSTRUCTION PHASE

WORK SUMMARY CONTINUED

AREA 4

Miscellaneous wall tile is in progress

Ceiling grid installation is in progress

Millwork installation is in progress

Lighting installation is in progress


Interior storefront installation is in progress

AREA 5

Lighting installation is in progress

Kitchen tile is in progress

Epoxy flooring is in progress

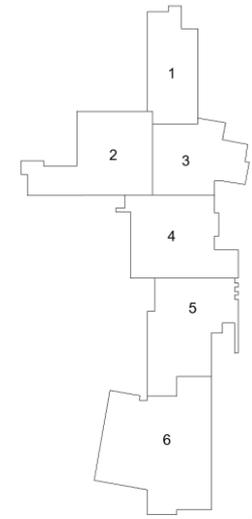

HS PHASE 1 AND 2 – CONSTRUCTION PHASE


WORK SUMMARY CONTINUED

AREA 6 PA WING

Acoustical wall panel installation is in progress

Light installation is in progress


Permanent power and HVAC has been turned on.

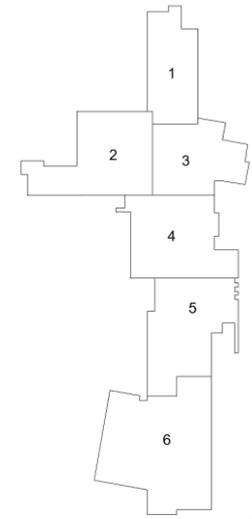

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




EXTERIOR – WEST PARKING / DROP-OFF LANE



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




SPEED PATHFINDERS KITCHEN / APARTMENT SKILLS AREA

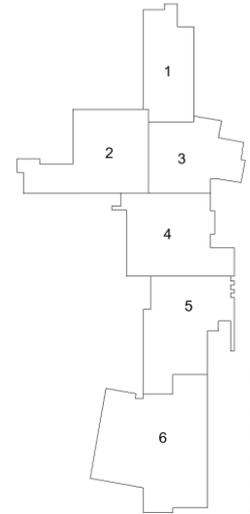

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




SPED CLASSROOM



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




SPED HALLWAY



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




GYMNASIUM

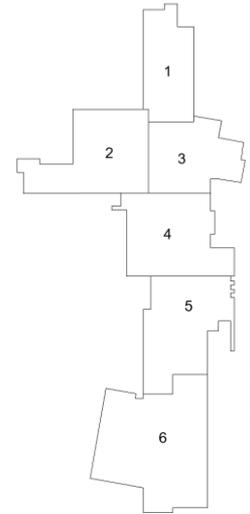

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




PE LOCKERROOM



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




COMMON AREA HALLWAY | FIRST FLOOR



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




COMMON AREA | FIRST FLOOR



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT SEATING OUTSIDE OF PRESENTATION



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




PRESENTATION ROOM

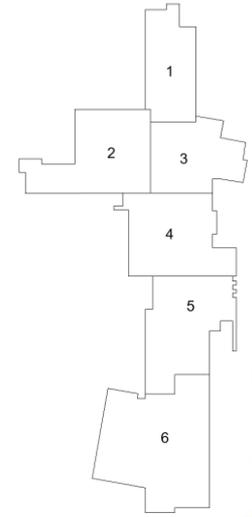

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




BOYS RESTROOM



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




SCIENCE LAB



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




SCIENCE CLASSROOM



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




FIRST FLOOR SCIENCE HALLWAY

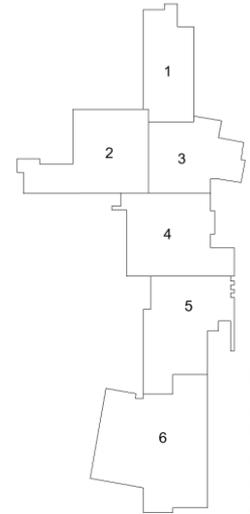

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




VISUAL ARTS SCULPTURE CLASSROOM | KILNS



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




GREENHOUSE



HS PHASE 1 AND 2 - CONSTRUCTION PHASE




NORTH STAIRWELL



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




COMMON AREA | SECOND FLOOR

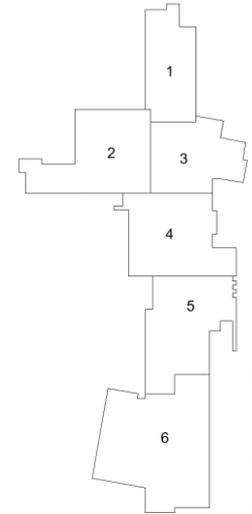

HS PHASE 1 AND 2 - CONSTRUCTION PHASE




TEACHER SUITE | SECOND FLOOR

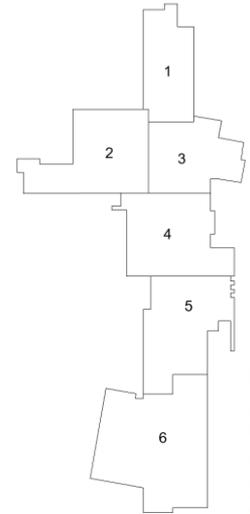

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




MEDIA CENTER STORAGE ROOM

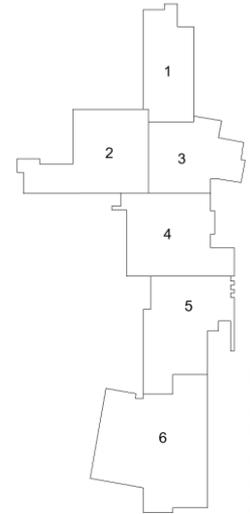

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




MEDIA CENTER

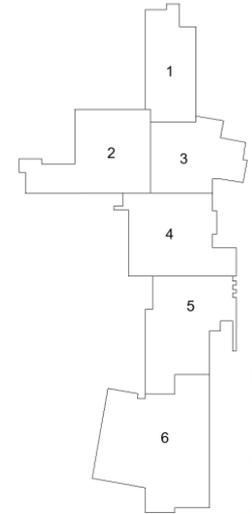

HS PHASE 1 AND 2 - CONSTRUCTION PHASE




STUDENT CENTER | SECOND FLOOR

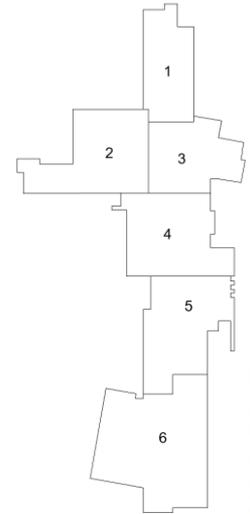

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT CENTER | FIRST FLOOR

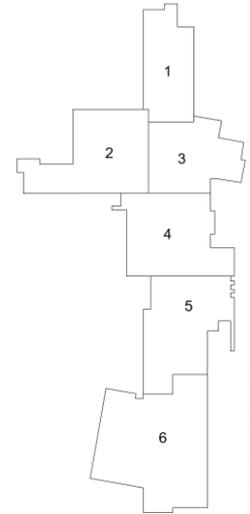

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT CENTER | PIONEER PERCH

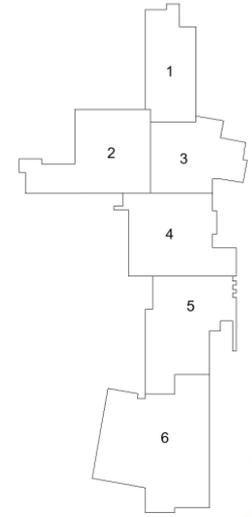

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT CENTER | STAIRWAY



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT CENTER | TROPHY DISPLAYS

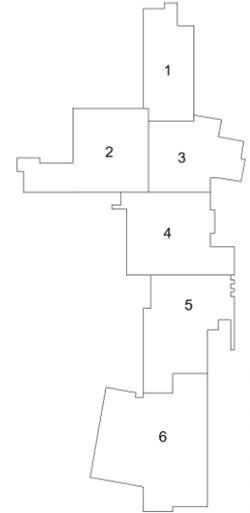

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




STUDENT CENTER | SERVERY LINES

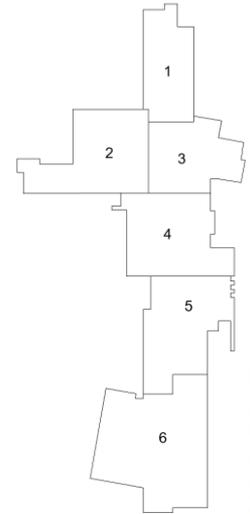

HS PHASE 1 AND 2 - CONSTRUCTION PHASE




FACS | CULINARY CLASSROOM

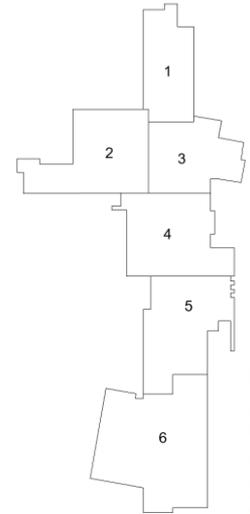

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




GUIDANCE LOBBY

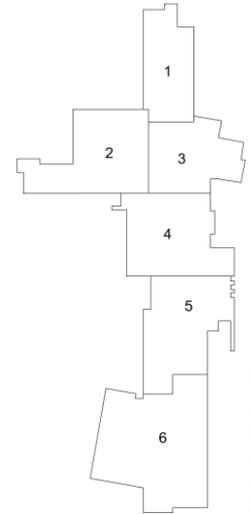

HS PHASE 1 AND 2 - CONSTRUCTION PHASE




TEACHER SUITE | FIRST FLOOR

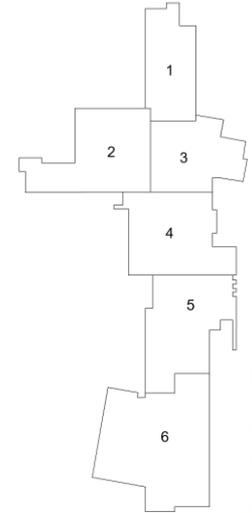

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




RECEPTION DESK

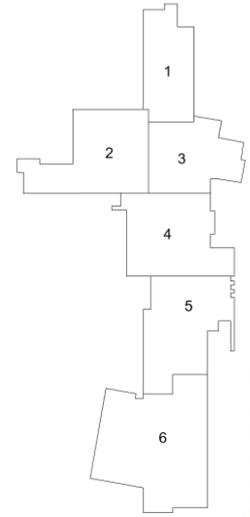

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




ATTENDANCE OFFICE

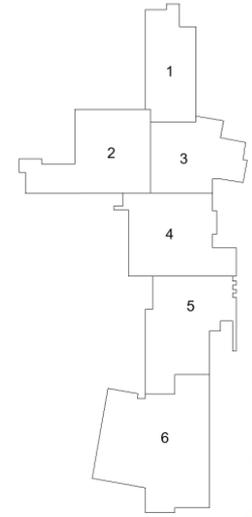

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




PA WING COMMON AREA

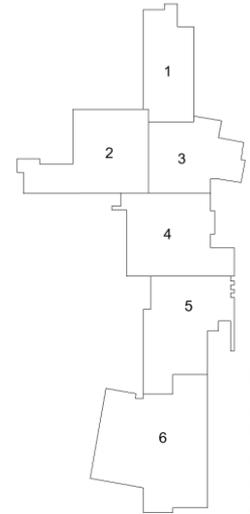

HS PHASE 1 AND 2 - CONSTRUCTION PHASE




PA WING COMMON AREA / PRACTICE ROOMS

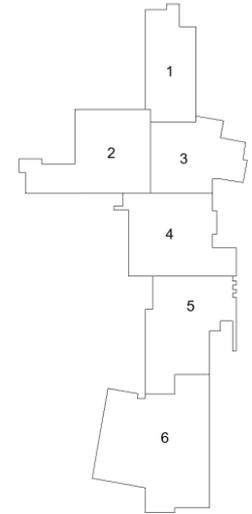

HS PHASE 1 AND 2 – CONSTRUCTION PHASE




PA WING PRACTICE ROOMS



HS PHASE 1 AND 2 – CONSTRUCTION PHASE




PA WING DRAMA CLASSROOM

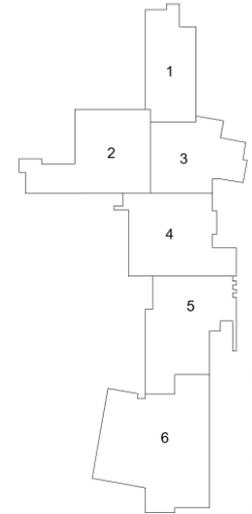

HS PHASE 1 AND 2 – CONSTRUCTION PHASE



PA WING LARGE BAND ROOM | ACOUSTICAL WALL PANELS

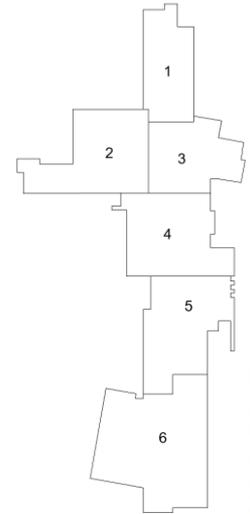

HS ATHLETICS PHASE 1 DD PHASE

SPS Athletics Phase 1 improvements on the existing High School campus that include new gym, weight room, wrestling, locker rooms, indoor practice spaces, outdoor practice field, and associated supports spaces. Project is in Construction Documentation (CD) Phase.

- 505 Architects has begun CD Phase with a 75% Construction Documentation Phase SPS review meeting the week of 3/9.
- 505 Architects is working with SPS on development of the FF&E Package for SPS Athletics Phase 1.
- SPS Athletics Phase 1 Early Demolition and Abatement Package bid opening occurred on 1/29 with good bidder turnout. BOE consideration to award bid at the February BOE meeting with abatement and demolition of West Gym and City Gym anticipated to begin in second half of February, and existing High School in June 2026.
- SPS Athletics Phase 1 Early Civil and Landscape Package scheduled to issue on 2/20 and Bid in March 2026 with April 2026 BOE consideration to award bid.
- SPS Athletics Phase 1 is scheduled to issue on 4/17 and Bid in May 2026 and begin construction in June 2026.
- Field House Locker Room Renovation Package is schedule to issue on 2/11 for bidding and construction pending BOE approval to go to Bid. The intent is for this work to be completed over the Summer 2026.





STILLWATER PUBLIC SCHOOLS

