



**BOND PROJECT UPDATES  
AS OF: JULY 13, 2026**

**BASEBALL AND SOFTBALL STADIUMS – FIELD LIGHTING UPGRADE**

**Contracts Awarded to:**

Engineer:	Stridde, Callins & Associates, Inc.
Contractor:	Musco Sports Lighting, LLC

**Project Timelines:**

Board Approved Contracts/Purchases:	April 20, 2026
Contracts Awarded & Purchase Orders Issued:	April 21, 2026
Project Start Date:	TBD
Estimated Project Completion Date:	TBD

**Project Updates:**

Administration worked with Stride, Callins, & Associates (MEP Engineering Firm) to develop a scope of work to upgrade the existing Baseball & Softball Field Lighting to LED. The best value to the District is to retrofit using the existing poles, therefore, the District solicited a purchasing cooperative contract quotation from Musco Sports Lighting, LLC. Administration and the engineer have approved the submittal package, and it will take 8-10 weeks to manufacture and ship the materials.

**PHIL DANAHER STADIUM – STADIUM RENOVATION & PRESS BOX REPLACEMENT**

**Contracts Awarded to:**

Architect:	Rawley McCoy & Associates
Contractor:	B.E. Beecroft Company

**Project Timelines:**

Board Approved Contracts/Purchases:	December 2, 2025
Contracts Awarded & Purchase Orders Issued:	December 5 2025
Project Start Date:	December 8, 2025
Estimated Project Completion Date:	August 31, 2026


**Project Updates:**

The project commenced on December 8, 2025 and will be completed by August 31, 2026. The old press box was demolished on December 19, 2025. The press box elevator tower brick installation and waterproofing are complete and the metal panels are onsite with installation starting in the coming weeks. The press box is constructed, waterproofing, framing, and glass installation are complete, and interior finish out is ongoing. The fence replacement on the interior of the stadium is complete, and the exterior estate fencing installation is 90% complete. All restroom expansions are dried in, and plumbing and electrical rough-in is underway. Stadium entrance steel structures and brick installations are complete and the roofing and finish out will begin in the coming weeks. Site work and final construction cleanup have begun.

**Project Photos:**





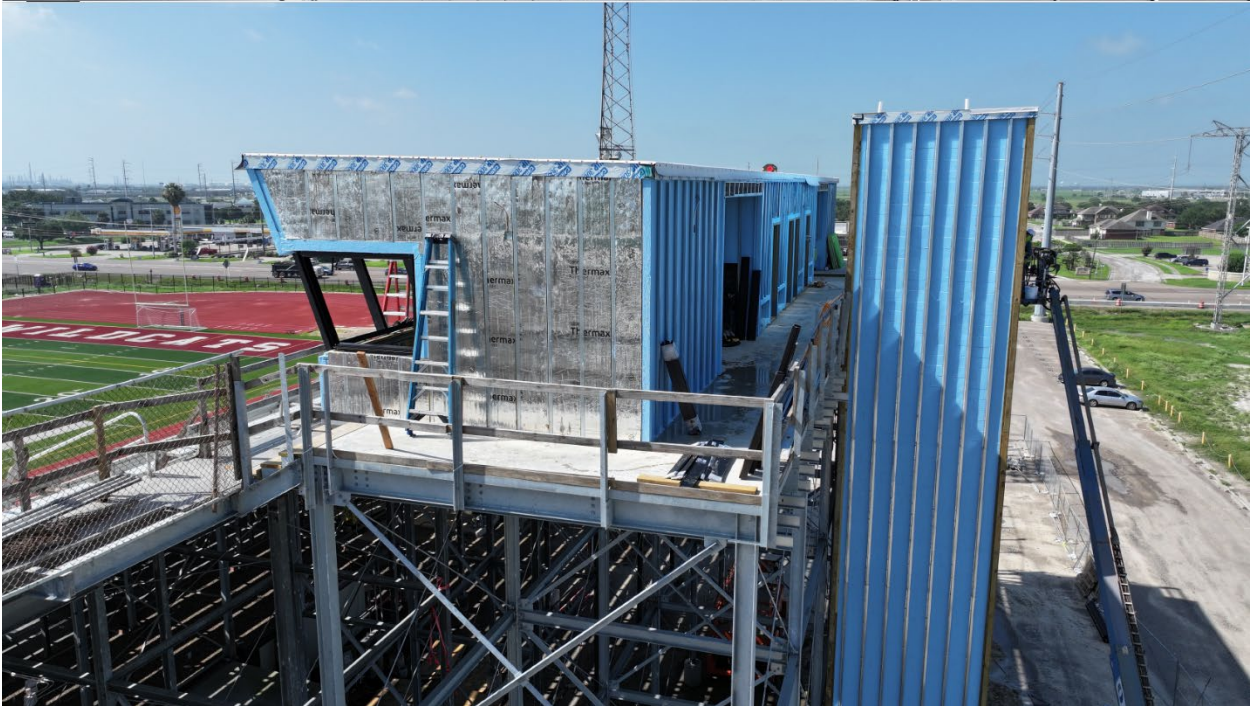

**PHIL DANAHER STADIUM – SCORE BOARD REPLACEMENT**

**Contracts Awarded to:**

Independent Design Representative:	Stridde, Callins & Associates, Inc. Wilkerson & Sanders, Inc.
---------------------------------------	--

Contractor:	Nevco Sports, LLC
-------------	-------------------

**Project Timelines:**

Board Approved Contracts/Purchases:	July 14, 2025
Contracts Awarded & Purchase Orders Issued:	August 5, 2025
Estimated Project Start Date:	January 1, 2026
Estimated Project Completion Date:	July 31, 2026

**Project Updates:**

The board approved the contractor selections and contract with Nevco Sports, LLC on July 14, 2025. The old scoreboard was demolished on April 13, 2026. The new scoreboard structure is complete. The electrical and connectivity installations are ongoing. The estimated project completion date is July 31, 2026.

**Project Photos:**





**GENERAL PLANNING COSTS**

*All Bond 2024 Projects*

**Legal Services:**

**Walsh Gallegos**

*Estimated expenditures \$20,000*

Administration continues to work closely with legal counsel to negotiate and finalize contracts for the Bond 2024 program. Utilizing the assistance of legal counsel ensures that the Bond 2024 program is compliant with all applicable laws during every phase.

**Architect Services:**

**Rawley McCoy and Associates, PLLC**

Rawley McCoy and Associates’ (RMA) contract was awarded at the May 13, 2024 Board Meeting. Future updates on RMA’s progress can be found on the specific projects updates above.

**Civil Engineering Services:**

**York Engineering**

*Estimated expenditures \$40,000*

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering’s progress can be found on the specific projects updates above.

**MEP Engineering Services:**

**Stridde, Callins & Associates, Inc.**

*Estimated expenditures \$75,000*

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

**Structural Engineering Services:**

**Wilkerson & Sanders, Inc**

*Estimated expenditures \$25,000*

Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

**Geotechnical Engineering and Construction Material Testing Services:**

**Intertek PSI**

*Estimated expenditures \$25,000*

Bond 2024 contracts were awarded at the June 24, 2024 Board Meeting. Administration will begin scheduling these services as needed throughout project design and implementation.
