



# MAY 2026 MONTHLY PROGRESS REPORT

## Riverside Public School District 96

### Ames Elementary School

86 Southcote Rd, Riverside, IL, 60546

### Hauser J. High School

65 Woodside Rd, Riverside, IL, 60546

### Blythe Park School

735 Leesley Rd, Riverside, IL, 60546

### **Vistara Construction Services, Inc.**

728 West Jackson Boulevard, Suite 526

Chicago, IL 60661

[www.vistara.com](http://www.vistara.com)



# Riverside Public School District 96

3340 S Harlem, Riverside IL 60546


2026 Summer Projects - Ames Elementary & Blythe Park Elementary Schools



MAY 2026

## Ames Elementary & Blythe Park Elementary School

## 2026 Summer Projects

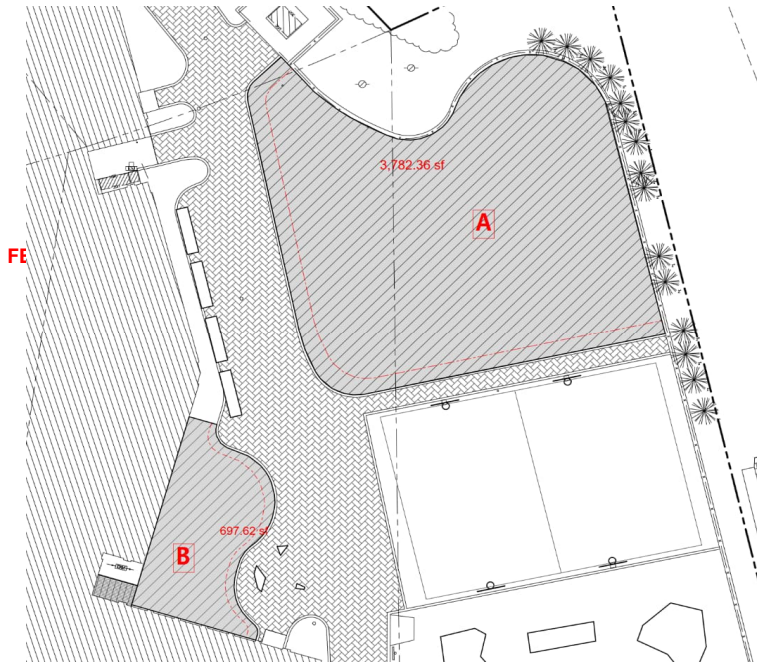


### Ames Elementary School Playground Surface Improvement Project:

Removal of the existing playground surface area, which includes:

1. Excavating and removing the existing playground surface
2. Installing new underdrainage per MWRD requirements
3. Backfilling and installing new playground surface materials.

**Note: To be considered at a later time**

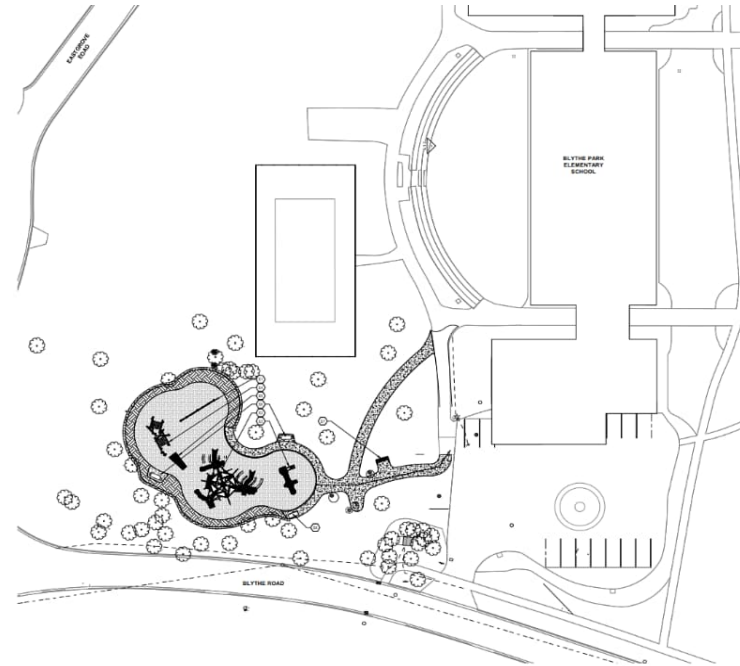

### Blythe Elementary School Playground Project:

Removal of the existing playground equipment, which includes:

1. Disposing the existing playground equipment
2. Surfacing, site drainage and other associated site work
3. Installing cobble paver curbing, site furniture, and playground equipment

Construction is to commence the first week of June 2026 and will be substantially complete by early August 2026.

**GC: D&J Landscaping**

**Key Activities:**

1. Submitted all required pre-construction documents

# Riverside Public School District 96

3340 S Harlem, Riverside IL 60546

2026 Summer Projects- Hauser Junior High School



**MAY 2026**

## Hauser Junior High School | 2026 Summer Projects



### Hauser Junior High Cornice Tuckpointing Project:

Perform lintel restoration to the 3rd floor windows, which includes:

1. Removing stone heads and bearing stone units to expose steel lintels
2. For Lintels above windows: Clean, prime, paint, and install new flashing
3. Reinstalling stone head and bearing stone units.

Construction commenced in June 2026. GC to mobilize (deliver equipment) the first week. Substantial completion: August 2026

**GC: MBB Enterprise of Chicago, Inc.**

### Key Activities:

1. Submitted all required pre-construction documents
2. MBB is scheduled to commence operations on June 1, approximately 15 days ahead of Krull
3. MBB is scheduled to drop off boom lifts after school hours by June 1st.

### Hauser Junior High Windows Replacement Project:

Replacement of the existing window units, which includes:

1. Removing and disposing of all windows
2. Installation of new aluminum insulated windows

Construction to commence in June 15, 2026. GC to deliver fence, equipment, storage and materials mid-June. Substantial completion: August 2026

**GC: Krull Window Company**

### Key Activities:

1. Submitted all required pre-construction documents
2. Submitted a site operations plan for the location of their storage container/ Porta-Potty.
3. Krull to scheduled to have the mockup setup by June 15.
