



BUB Report

Building Update Brief

Facilities and Grounds

&

Summer Construction Projects

July 9th, 2026

Andrew Nordstrom
Director of Facilities, Grounds, and Transportation

Table of Contents

1. Title Page
2. Table of Contents
3. Purpose
4. HS and DO Office Remodel
5. HS and DO Office Remodel Continued
6. Auditorium Stage Lighting Upgrade
7. Exterior Building Sealing and Caulking
8. HS Gym Floor Refinish
9. PreSchool Playground Roof Drainage
10. CEJ HVAC and Boiler Replacement
11. CEJ Outdoor Classroom
12. Rec Pool Center Locker Room Floor Refinish
13. HS Cooler and Freezer Replacement
14. CEJ Door 12 Sidewalk and Wall Fix
15. End/Questions



Purpose

The purpose of this presentation is to provide the Superintendent and Board of Education updates on Facilities and Grounds and Summer Construction Updates.



High School and District Office Remodel


Current Update:

Demo is complete and Framing of the walls will start on Monday 7/13.

Electrical (High and Low Voltage) Rough-ins during next week.

Framing inspection will follow completion of framing.

After framing they will sheetrock, mud, and tape.

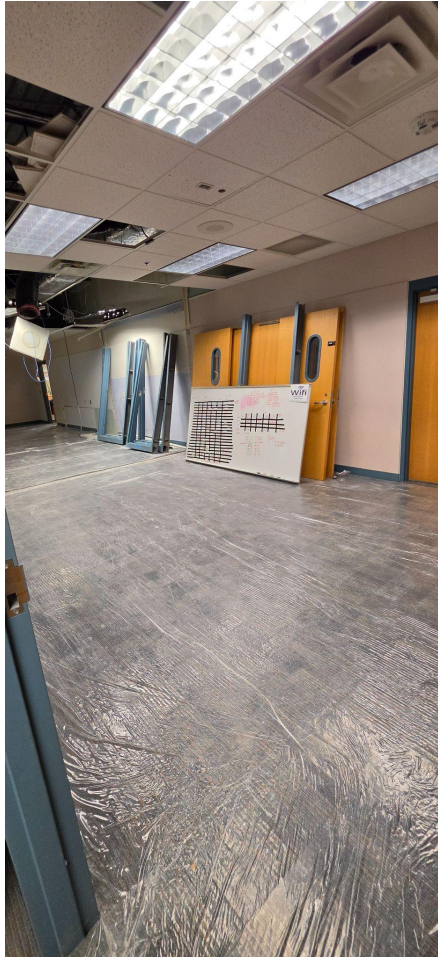

High School and District Office Remodel Continued




High School Auditorium Stage Lighting Upgrade

Current Update:

Light Installation is complete.

Controls are complete.

Working on a schedule training date for Rush City Staff.

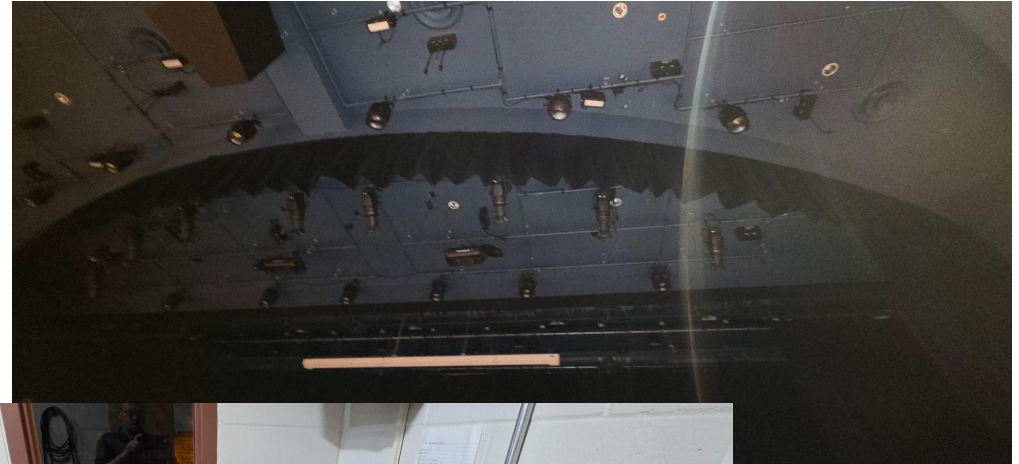

Exterior Building Caulking and Tuckpointing

Current Update:

The company will be back in middle of July to work on Tuckpointing.

Caulking is complete. Will caulk CEJ Door 12 new concrete when back onsite.





High School Gym Refinish

Current Update:

FLR Sanders are currently sanding base floor. All lines have been removed.

Damaged area has been fixed.

Next steps is to continue with sanding and layout of lines.

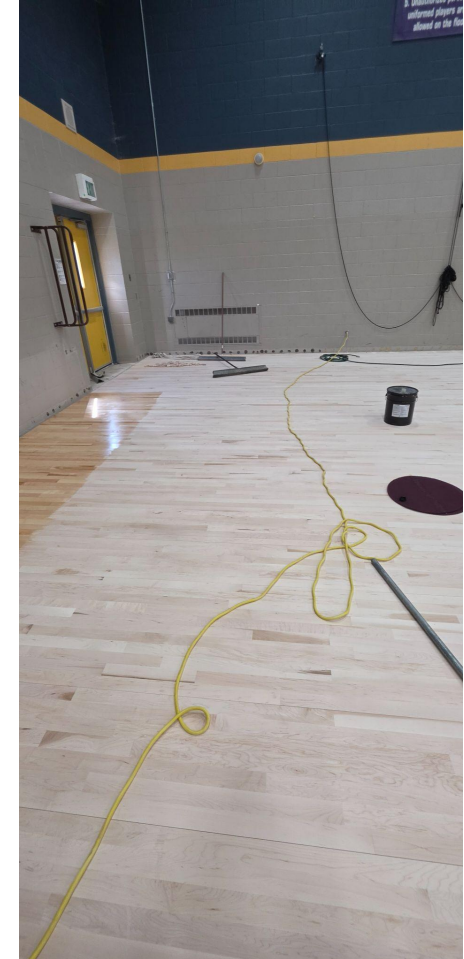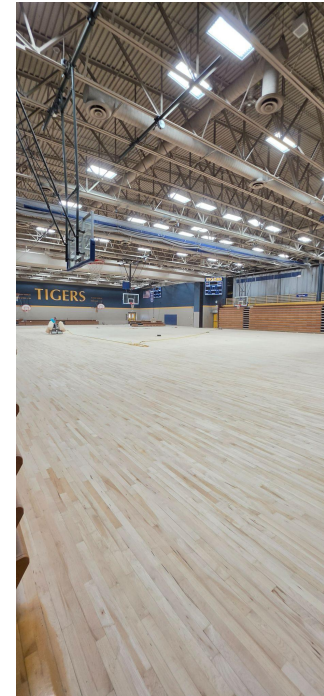


CEJ Preschool Playground Roof Drainage

Current Update:

Project is complete.

New Drain Basin and Drain Line are working as it should.

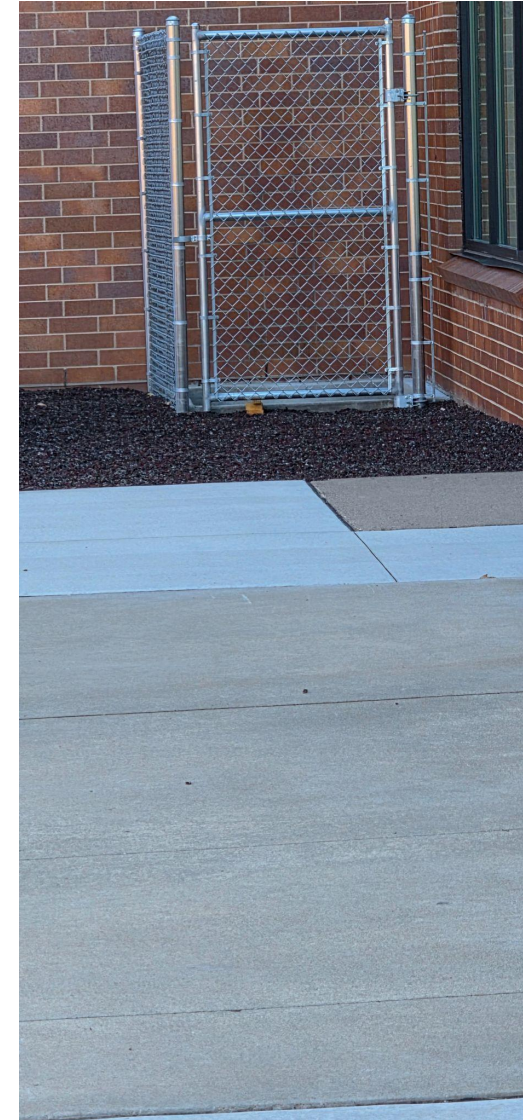

CEJ HVAC and Boiler Replacement

Current Update:

- ❖ Project is underway.
- ❖ Equipment has been ordered.
- ❖ Floor protection has been set for construction.
- ❖ Working on Heating Equipment Rebates.
- ❖ Construction will begin after summer is completed.
 - August - Start with ceilings to be removed piping to run in hallway and then reinstall ceilings.
 - August - Demo Old Boilers and Water Heaters.
 - August - Install Water Heaters
 - August and September - Install Boilers and Pumps



CEJ Outdoor Classroom

Current Update:

Shade Project has been started

Footings for shade structure is underway.

Installation of shade structure and shade will happen this week and next week.

Concrete pad will be installed after shade project is complete.







Rec Pool Center Locker Room Floor Refinish

Current Update:

Floor refinish is complete.

Due to safety concerns another coating has been added to floor to make it less slippery.

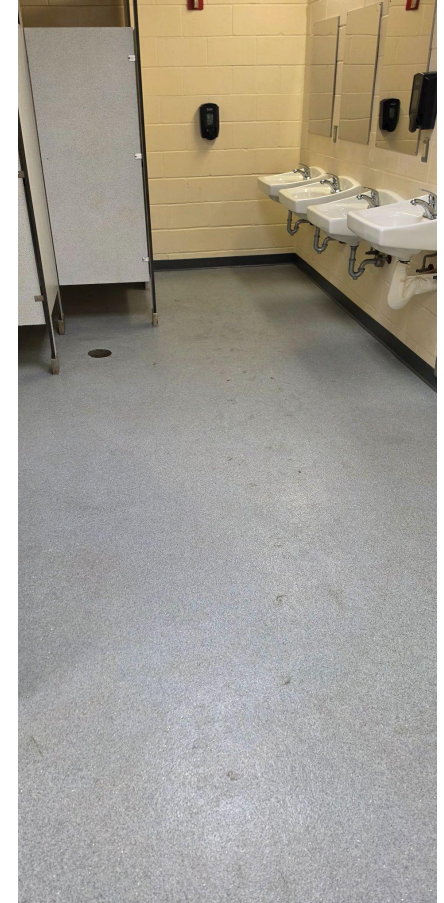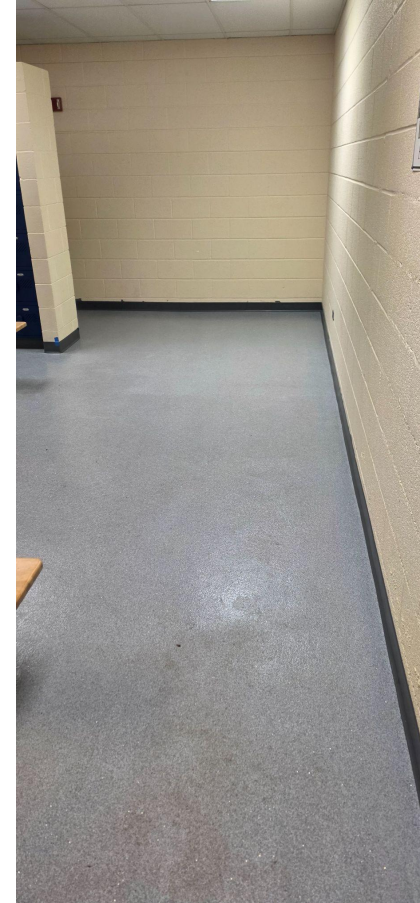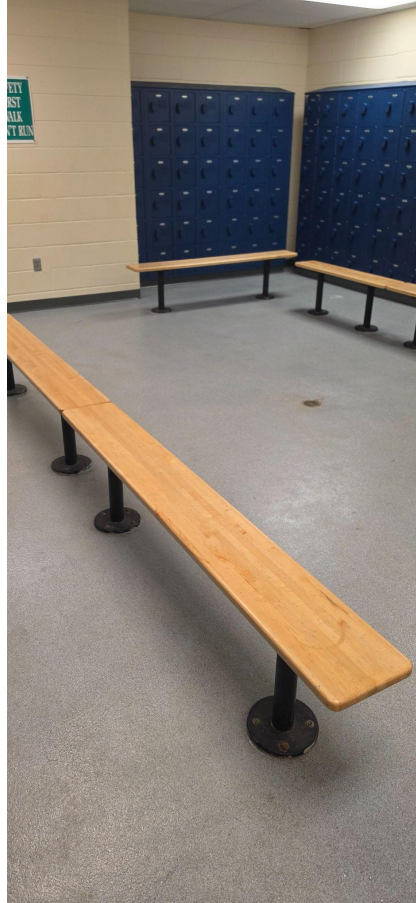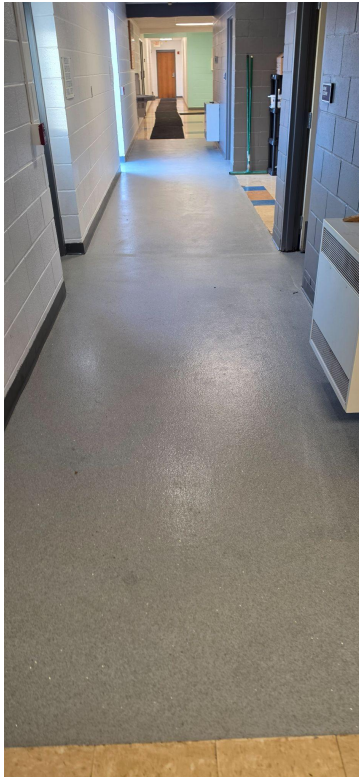

HS Cooler and Freezer Replacement

Current Update:


Demo of old equipment is complete.

Measurements have been taken and panels are in process of being created.

Once panels are completed they will be installed.

Installation of new panels is scheduled for end of July.

Received and Installed new refrigerator and hand wash sink.

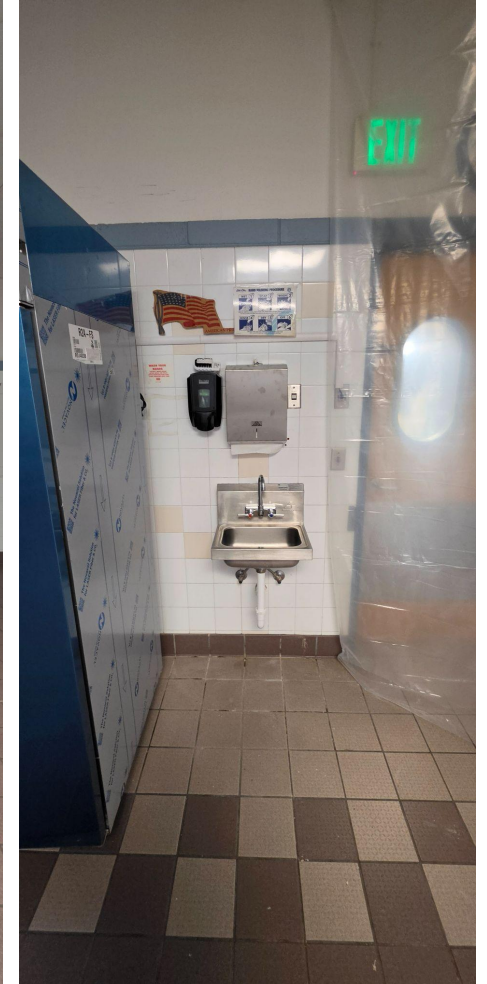


CEJ Door 12 Sidewalk and Wall Fix

Current Update:

Demo'd old sidewalk.

Installed new concrete sidewalk.

Repaired brick and tuck pointed damaged areas.

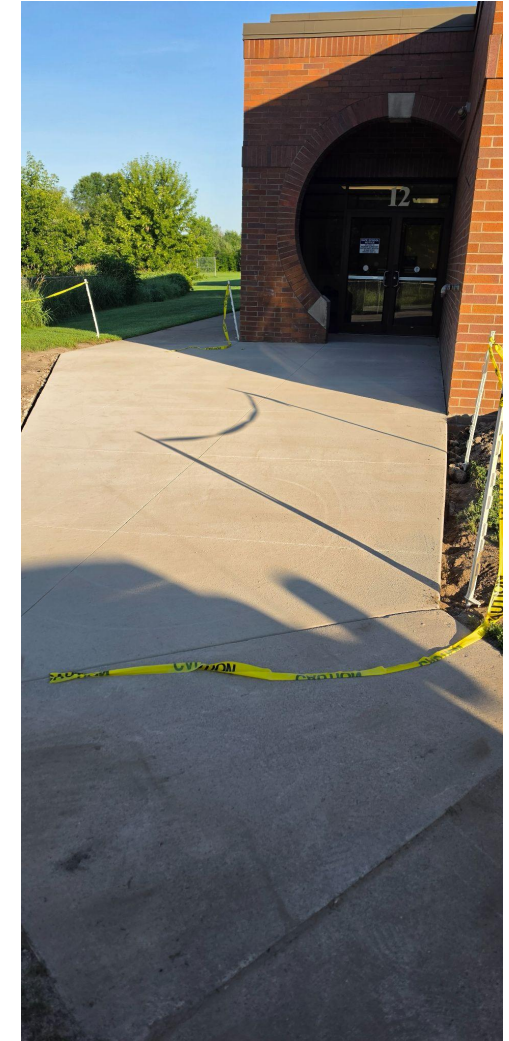

End of Presentation

Questions???

Thank you!!!

