

ROOF PROGRESS REPORT THROUGH 07-13-2026

Contact:	Keri Hacker (507) 273-2689 khacker@tremcoinc.com
Inspector:	Thomas Fritz Jr (507) 606-2861 tfritzjr2128@gmail.com
Project Manager:	Mike Kerker (319)-277-9355 mike@blackhawkroof.com
Contractor:	Black Hawk Roof Company
Foreman: (Translator)	Angel Palofox (817)-441-3919

Areas of Work: Roof Area 6 & 7

- 45 mil KEE fleece-backed membrane adhered in membrane adhesive (Roof Area 6 & 7)
- ¼" prime coverboard adhered in low-rise adhesive over insulation (Roof Area 6 & 7)
- 1-½" isocyanurate insulation board mechanically attached over existing insulation board (Roof Area 6 & 7)


Notes:

- Sheet metal crew to install scuppers drains after completion of roofing membrane

Issues and Corrections:

- Identified and replaced 124 square feet of wet insulation (Roof Area 5, 6, & 7)
- Roof area #5 unit removal caused leakage around wrestling room ceiling.
- Stone mason to fix leak found on the wall of roof area 12


Project Maps:

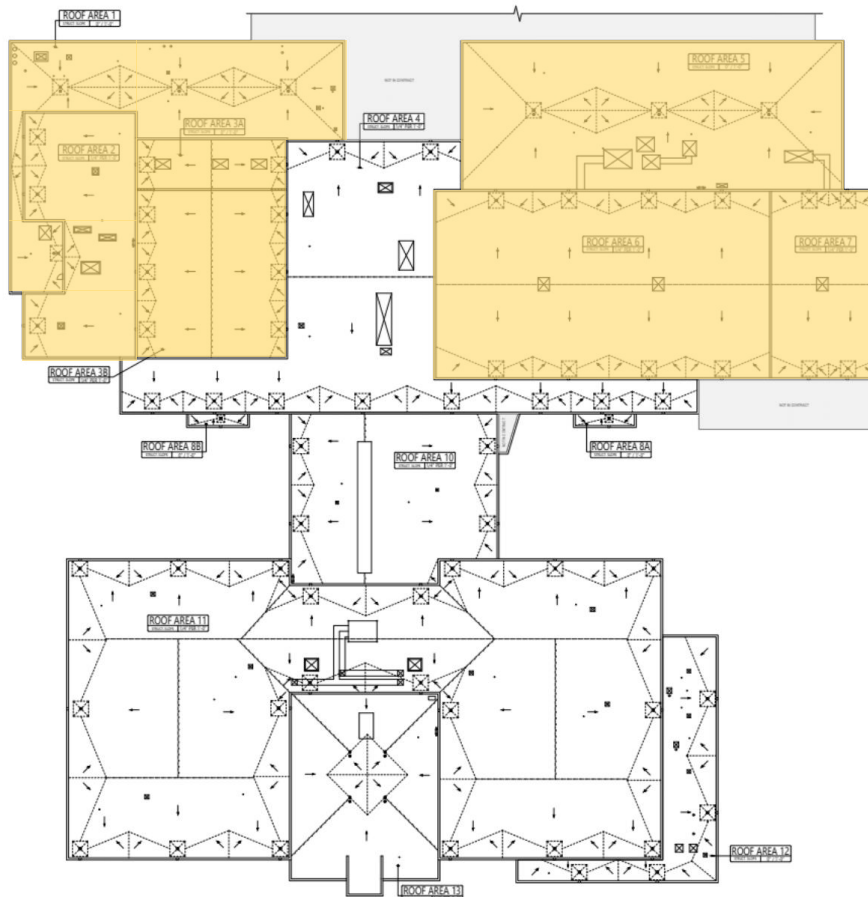

Roof Area 100% Completed



Roof Area primarily completed



Roof Area started

ROOF PROGRESS REPORT THROUGH 07-13-2026

ROOFING SCHEDULE		
ROOF AREA	STATUS	SCHEDULE
#1	90% COMPLETE	WEEK OF 6/22
#2	90% COMPLETE	WEEK OF 6/22
#3A	90% COMPLETE	WEEK OF 6/15
#3B	90% COMPLETE	WEEK OF 6/15
#5	90% COMPLETE	WEEK OF 7/06
#6	90% COMPLETE	WEEK OF 7/06
#7	90% COMPLETE	WEEK OF 7/13

ROOF PROGRESS REPORT THROUGH 07-13-2026



60 Mil KEE fleece-backed membrane adhered
in membrane adhesive on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



Membrane insulation at roof area #5 has been completed around roof curbs, mechanically fastened with cap nails.

ROOF PROGRESS REPORT THROUGH 07-13-2026



Roof area #5 unit removal caused
leakage around wrestling room ceiling.

ROOF PROGRESS REPORT THROUGH 07-13-2026



Low-rising adhesive applied prior to dens
prime board setting on roof area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



45 Mil KEE fleece-backed membrane
seams water-tight on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



45 Mil KEE fleece-backed membrane
seams water-tight on Roof Area #7

ROOF PROGRESS REPORT THROUGH 07-13-2026




45 Mil KEE fleece-backed membrane adhered in
membrane adhesive on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



Drain and Sump Detail: KEE membrane is sealed to ensure watertight connection around drain on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026

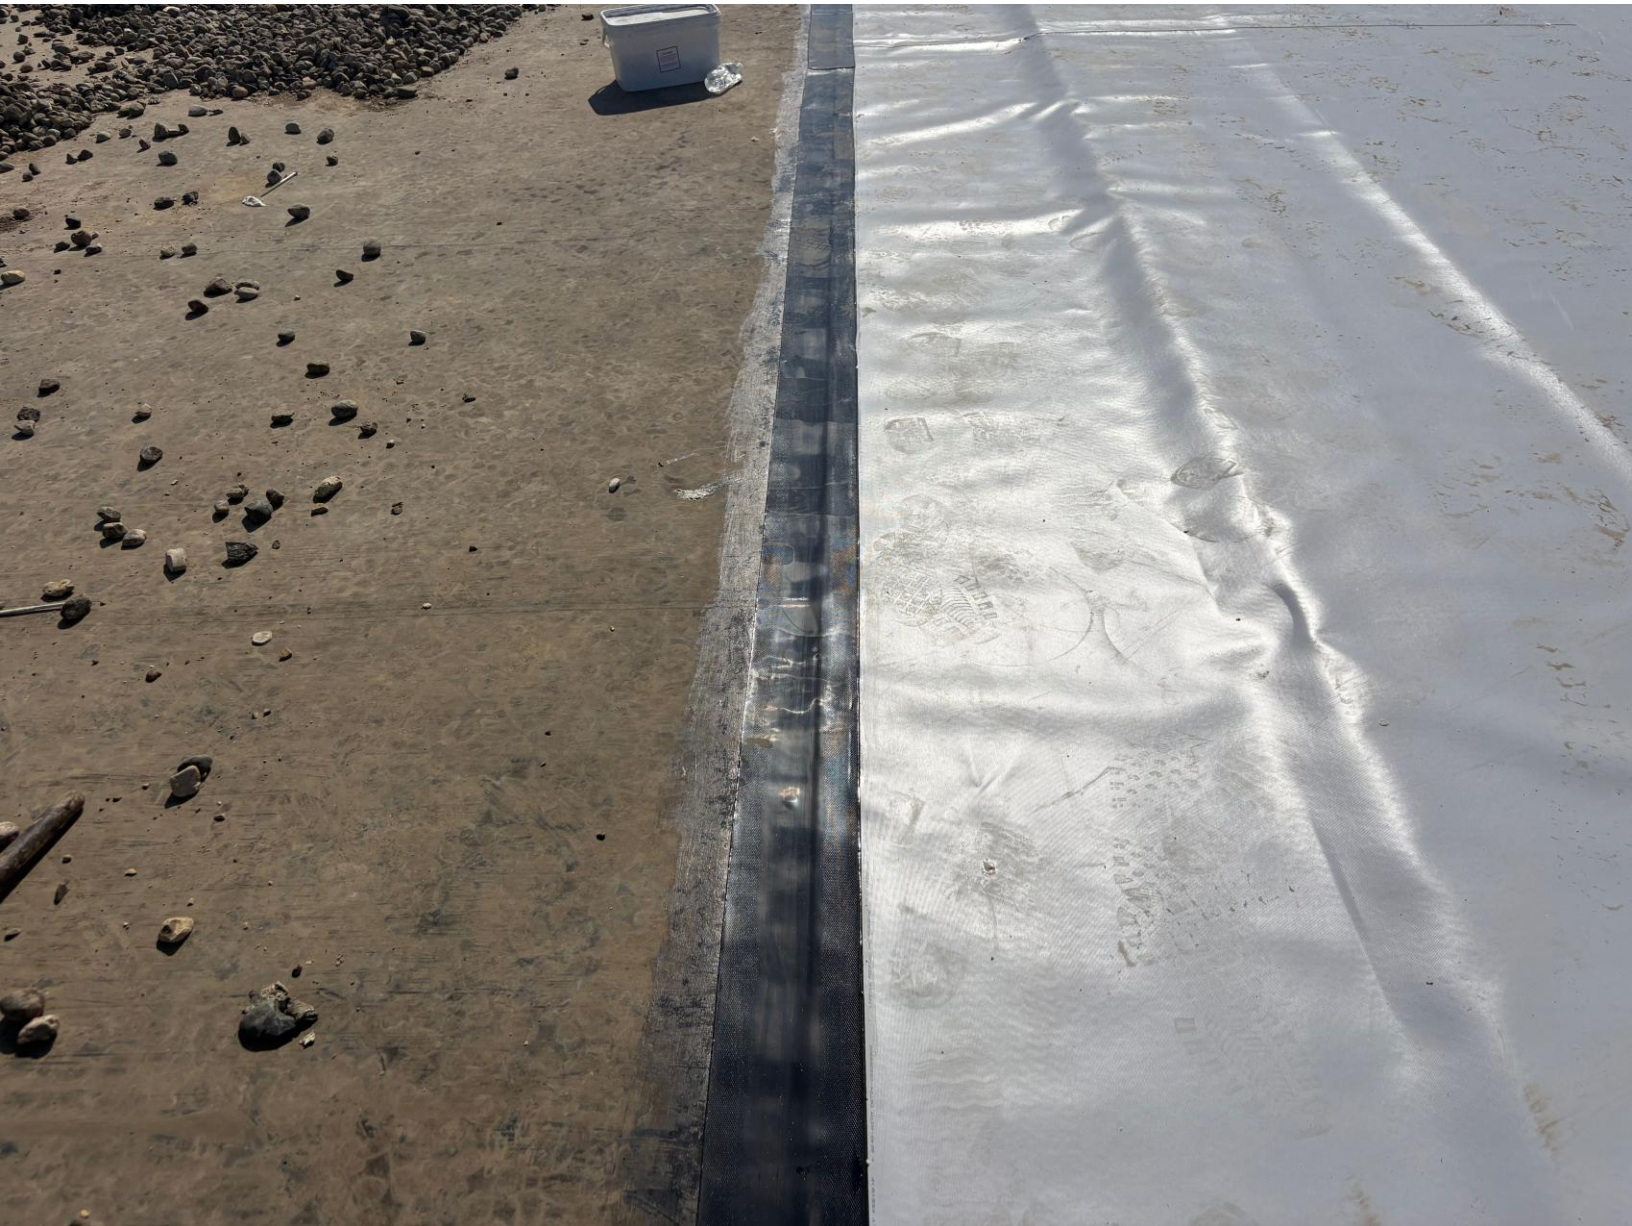

Tied off 45 Mil KEE fleece-backed membrane adhered in membrane adhesive to existing roof membrane on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



$\frac{1}{4}$ " prime coverboard adhered in low-rise adhesive
over insulation coverboard on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



Unit removal: Tied off open roof area
prior to storm on roof area #5

ROOF PROGRESS REPORT THROUGH 07-13-2026



1-1/2" Isocyanurate insulation board mechanically attached
over existing insulation with fast adhesive for ISO
coverboard on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



26 square feet of wet insulation found
on Roof Area # 6

ROOF PROGRESS REPORT THROUGH 07-13-2026



Daily weld test

ROOF PROGRESS REPORT THROUGH 07-13-2026



45 Mil KEE fleece-backed membrane adhered in
membrane adhesive on Roof Area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



1-1/2" Isocyanurate insulation board mechanically
attached over existing insulation with fast adhesive for
ISO coverboard on Roof Area #7

ROOF PROGRESS REPORT THROUGH 07-13-2026



Lawn temporarily raked. Sheet metal crew to utilize lawn to transport material roof

ROOF PROGRESS REPORT THROUGH 07-13-2026



Concrete pads placed around perimeter of unit
to capture condensate on roof area #6

ROOF PROGRESS REPORT THROUGH 07-13-2026



1-1/2" Isocyanurate insulation board mechanically
attached over existing insulation with fast adhesive for
ISO coverboard on Roof Area #7

ROOF PROGRESS REPORT THROUGH 07-13-2026



Flashing detail water-tight to curb with
termination far fastening the membrane
on roof area #5

ROOF PROGRESS REPORT THROUGH 07-13-2026



45 Mil KEE fleece-backed membrane adhered in
membrane adhesive on Roof Area #7
