



APRIL 2026 MONTHLY PROGRESS REPORT

Riverside Public School District 96

Ames Elementary School

86 Southcote Rd, Riverside, IL, 60546

Hauser J. High School

65 Woodside Rd, Riverside, IL, 60546

Blythe Park School

735 Leesley Rd, Riverside, IL, 60546

Vistara Construction Services, Inc.

728 West Jackson Boulevard, Suite 526

Chicago, IL 60661

www.vistara.com



Riverside Public School District 96

3340 S Harlem, Riverside IL 60546


2026 Summer Projects - Ames Elementary & Blythe Park Elementary Schools



APRIL 2026

Ames Elementary & Blythe Park Elementary School

2026 Summer Projects

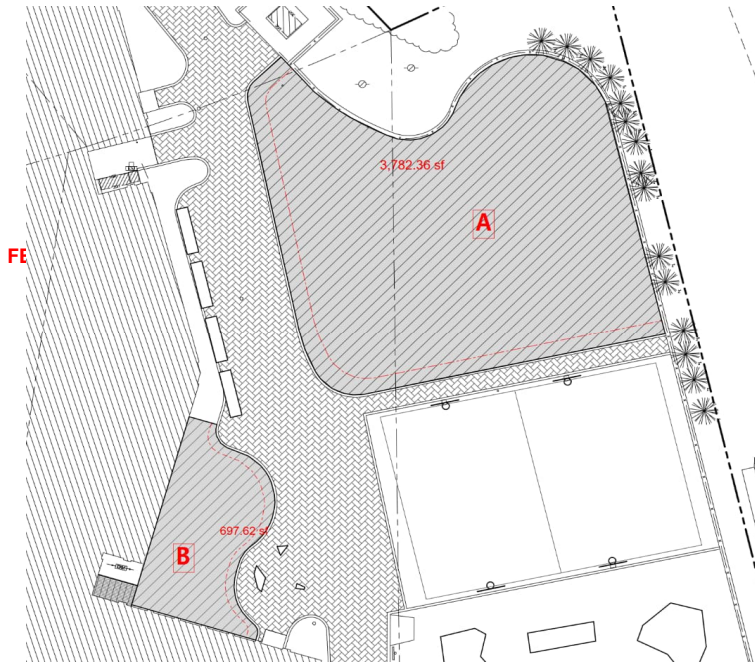


Ames Elementary School Playground Surface Improvement Project:

Removal of the existing playground surface area, which includes:

1. Excavating and removing the existing playground surface
2. Installing new underdrainage per MWRD requirements
3. Backfilling and installing new playground surface materials.

Note: To be considered at a later time

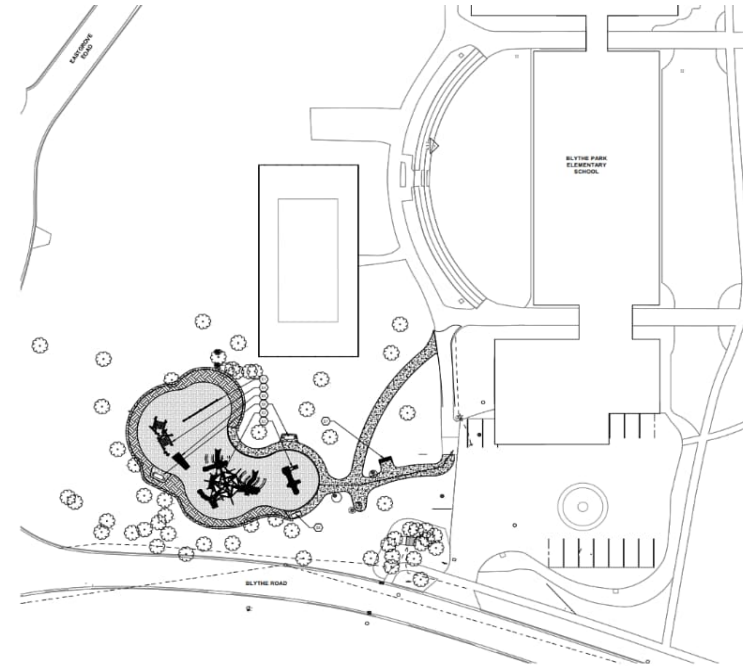

Blythe Elementary School Playground Project:

Removal of the existing playground equipment, which includes:

1. Disposing the existing playground equipment
2. Surfacing, curbing and other associated work
3. Installing new cobble paver curbing and playground equipment

Construction is anticipated to commence in June 2026 and be substantially completed by August 2026.

GC: D&J Landscaping

Key Activities:

1. Submitted all required pre-construction documents

Riverside Public School District 96

3340 S Harlem, Riverside IL 60546

2026 Summer Projects- Hauser Junior High School



APRIL 2026

Hauser Junior High School

2026 Summer Projects



Hauser Junior High Cornice Tuckpointing Project:

Perform lintel restoration to the 3rd floor windows, which includes:

1. Removing stone heads and bearing stone units to expose steel lintels
2. For Lintels above windows: Clean, prime, paint, and install new flashing
3. Reinstalling stone head and bearing stone units.

Construction is anticipated to commence in June 2026 and be substantially completed by August 2026.

GC: MBB Enterprise of Chicago, Inc.

Key Activities:

1. Submitted all required pre-construction documents
2. MBB is scheduled to commence operations on June 1, approximately 15 days ahead of Krull

Hauser Junior High Windows Replacement Project:

Replacement of the existing window units, which includes:

1. Removing and disposing of all windows
2. Installation of new aluminum insulated windows

Construction is anticipated to commence in June 2026 and be substantially completed by August 2026.

GC: Krull Window Company

Key Activities:

1. Submitted all required pre-construction documents
2. Submitted a site operations plan for the location of the storage container/ Porta-Potty.
3. Krull is scheduled to commence operations on June 15.
