



**JACKY PYRCH**  
*Greenhouse Specialist*

Office 1.800.476.9715 x 1390  
Email [jpyrch@farmtek.com](mailto:jpyrch@farmtek.com)

**HEAD QUARTERS**  
1395 John Fitch Blvd, South Windsor, CT 06074

**USA PLANT**  
18th Ave SW, Dyersville, IA 52040



Corporate  
703 Hebron Avenue, Floor 3, Glastonbury, CT 06033  
p: 1.860.760.0046 • f: 1.888.958.1393 • www.clearspan.com



Customer ID: 9011502  
Quote Number: 1014286

**QUOTE**

Sourcewell Contract #: 091319-CSS

Page: 1 of 4

|  |   |
|--|---|
| <p><b>Quote To:</b><br/>HARRY LAU<br/>LIVONIA PUBLIC SCHOOLS<br/>15125 FARMINGTON RD<br/>LIVONIA MI 48154-5413<br/>UNITED STATES</p> <p>Phone: <b>7348128597</b><br/>hlau@livoniapublicschools.org</p> <p><b>Sales Person:</b> JACKY PYRCH<br/><b>Fax:</b> 800-457-8887<br/>JPYRCH@FARMTEK.COM</p> | <p><b>Ship To:</b><br/>LIVONIA PUBLIC SCHOOLS<br/>15125 FARMINGTON RD<br/><br/>LIVONIA, MI 48154-5413</p> <p><b>Date:</b> 4/20/2021<br/><b>Expires:</b> 5/20/2021</p> |
|--|---|

USD

| Line  | Part     | Description   | Expected Qty | Unit Price | Ext. Price |
|---|----------|---|--------------|------------|------------|
| 1   | 200106   | GROWSPAN SERIES 2000 GABLE-TOPPED COMMERCIAL GREENHOUSE 35'W X 60'L, ENGINEERED | 1.00         | 43,887.59  | 43,887.59  |
| <p><i>Project Size: (1) 35' X 60' GrowSpan Series 2000 Gable-Topped greenhouse<br/>Total Square Footage: 2100 sqft (35 x 60' footprint)<br/>Side Height: 10'<br/>10' column/truss spacing with heavy duty 4x4 inch square 8 gauge triple galvanized steel columns<br/>Stamped/Engineered for 20psf ground snowload + 115 mph ultimate windload, Category III<br/>--PLEASE CONFIRM LOAD WITH LOCAL ZONING ORDINANCE--</i></p> <p><i>Primary structural members (posts, trusses, purlins) are triple galvanized and fully enclosed (tubular). No partially enclosed members - C-channel, roll forming or press braking - allowed.<br/>Heavy duty base plate anchoring system with concrete anchors included. This system eliminates labor &amp; error associated with anchor posts that must be wet set into concrete + allows concrete to be poured &amp; cured prior to greenhouse delivery. Can be engineered to meet any snow/wind loads. Can be mounted to cylindrical pier footings (economical choice), grade beams or slabs.<br/>FarmTek includes the following items with every GrowSpan Series 1000 &amp; 2000 greenhouse purchase: framing for quoted doors, fans, coolers, vents + heavy duty "walk-in" gutters + condensate removal system + covering materials with appropriate fasteners, flashings, closure strips and sealants</i></p> <p><i>Clear 8mm twinwall polycarbonate to cover entire structure's cladding</i></p> |          |   |              |            |            |
| 2   | 100202   | ADA COMPLIANT ALUMINUM DOUBLE HUNG DOOR 3'X7'                                   | 2.00         | 3,833.52   | 7,667.04   |
| 3   | 115777NA | DURACOIL BASIC 24GA- 10X10 DOOR W/OPERATOR                                      | 1.00         | 3,378.75   | 3,378.75   |

Proposal reflects Sourcewell Pricing. Only available through the purchasing CoOp. PO must state Sourcewell contract # to qualify.



Corporate  
 703 Hebron Avenue, Floor 3, Glastonbury, CT 06033  
 p: 1.860.760.0046 • f: 1.888.958.1393 • www.clearspan.com



**Customer ID: 9011502**  
**Quote Number: 1014286**

**QUOTE**

Sourcewell Contract #: 091319-CSS

Page: 2 of 4

|    |          |  |      |           |           |
|----|----------|--|------|-----------|-----------|
| 4  | 700012   | CUSTOM GREENHOUSE DESIGN AND ENGINEERING - STAMPED DRAWINGS - PRICE WHEN ORDERED WITH MATERIALS  | 1.00 | 3,750.00  | 3,750.00  |
| 5  | WF4400   | 50' HOSE TROLLEY KIT   | 2.00 | 103.50    | 207.00    |
| 6  | 100202   | ROOF-ONLY SHADE SYSTEM 35'W X 60'L C/W RIDDER RW45 REVERSIBLE GEAR MOTOR + PUSH PULL DRIVE SYSTEM + SVENSSON SOLARO 40% SHADE MATERIAL- CUSTOM   | 1.00 | 6,948.99  | 6,948.99  |
| 7  | 112929   | IDRIVE FOR MOTOR 112925  | 1.00 | 485.10    | 485.10    |
| 8  | 116417   | IGROW 800 INTEGRATED W/LINK4 STANDARD PANEL  | 1.00 | 2,695.50  | 2,695.50  |
| 9  | 111142   | SENSOR INDOOR DIGITAL TEMP & HUMIDITY  | 1.00 | 314.10    | 314.10    |
| 13 | 116191   | 36" 1SP 115/208-230V DD 1/2HP SLANT WALL FAN   | 2.00 | 575.10    | 1,150.20  |
| 14 | 116600   | 24" EXHAUST FAN W/V-SP MOTOR 115V  | 1.00 | 332.10    | 332.10    |
| 15 | 113903MK | 30" 3100 SERIES MOTORIZED DAMPER KIT   | 1.00 | 199.10    | 199.10    |
| 18 | 113906MK | 54" 3100 SERIES MOTORIZED DAMPER KIT   | 3.00 | 629.10    | 1,887.30  |
| 21 | 103657P  | MODINE 140M BTU PDP GRNHOUSE HEATER - PROPANE  | 2.00 | 1,052.10  | 2,104.20  |
| 22 | 113104   | HEATER HANGER PKG (S750/S1000/S2000)   | 2.00 | 197.96    | 395.92    |
| 23 | 111939   | FAN 20" HORIZONTAL AIRFLOW 1/10HP 115V   | 4.00 | 144.16    | 576.64    |
| 24 | 700005   | GREENHOUSE INSTALLATION - THE CURRENT QUOTE TOTAL EXCLUDES PERMITS, INSPECTIONS, GRADE WORK, SITE PREP, FOUNDATION, FINISH FLOORING, UTILITIES TO THE SITE, BREAKER PANEL, UTILITIES TO THE EQUIPMENT, DRAINS, DOWNSPOUTS, INSTALLATION OF ANY ITEM NOT MENTIONED IN THIS PROPOSAL AND BUILD OUT INSIDE OF ANY QUOTED METAL BUILDING | 1.00 | 50,260.00 | 50,260.00 |

GREENHOUSE TOTAL + INSTALL 126,239.53  
 ESTIMATED - Freight 2,204.28

**Quote Total 128,443.81**

Proposal reflects Sourcewell Pricing. Only available through the purchasing CoOp. PO must state Sourcewell contract # to qualify.



Corporate  
 703 Hebron Avenue, Floor 3, Glastonbury, CT 06033  
 p: 1.860.760.0046 • f: 1.888.958.1393 • www.clearspan.com



Customer ID: 9011502  
 Quote Number: 1014286

**QUOTE**

Sourcewell Contract #: 091319-CSS

Page: 3 of 4

|    |        |  |      |           |           |
|----|--------|--|------|-----------|-----------|
| 24 | 700005 | GREENHOUSE INSTALLATION - THE CURRENT QUOTE TOTAL EXCLUDES PERMITS, INSPECTIONS, GRADE WORK, SITE PREP, FOUNDATION, FINISH FLOORING, UTILITIES TO THE SITE, BREAKER PANEL, UTILITIES TO THE EQUIPMENT, DRAINS, DOWNSPOUTS, INSTALLATION OF ANY ITEM NOT MENTIONED IN THIS PROPOSAL AND BUILD OUT INSIDE OF ANY QUOTED METAL BUILDING | 1.00 | 50,260.00 | 50,260.00 |
| 25 | 700015 | **OPTIONAL - PRICE EXCLUDED FROM TOTAL**FOUNDATION ENGINEERING-GREENHOUSE - PRICE WHEN ORDERED WITH MATERIALS  | 0.00 | 4,500.00  | 0.00      |
| 26 | 104251 | ** OPTIONAL - PRICE EXCLUDED FROM TOTAL** EZ-GROW 4X8 BENCH W/EXP METAL COMPLETE   | 0.00 | 221.36    | 0.00      |

*Please Note:  
 Additional Sales Tax will apply for materials and installation if the project is not tax exempt.*

Proposal reflects Sourcewell Pricing. Only available through the purchasing CoOp. PO must state Sourcewell contract # to qualify.



Corporate  
703 Hebron Avenue, Floor 3, Glastonbury, CT 06033  
p: 1.860.760.0046 • f: 1.888.958.1393 • www.clearspan.com



Customer ID: 9011502  
Quote Number: 1014286

**QUOTE**

Sourcewell Contract #: 091319-CSS

Page: 4 of 4

|                     |                   |
|---------------------|-------------------|
| Lines Total         | 126,239.53        |
| ESTIMATED - Freight | 2,204.28          |
| <b>Quote Total</b>  | <b>128,443.81</b> |

Quote Accepted By: \_\_\_\_\_ Date: \_\_\_\_\_

*Signature*




# PROJECTS





# PROJECTS

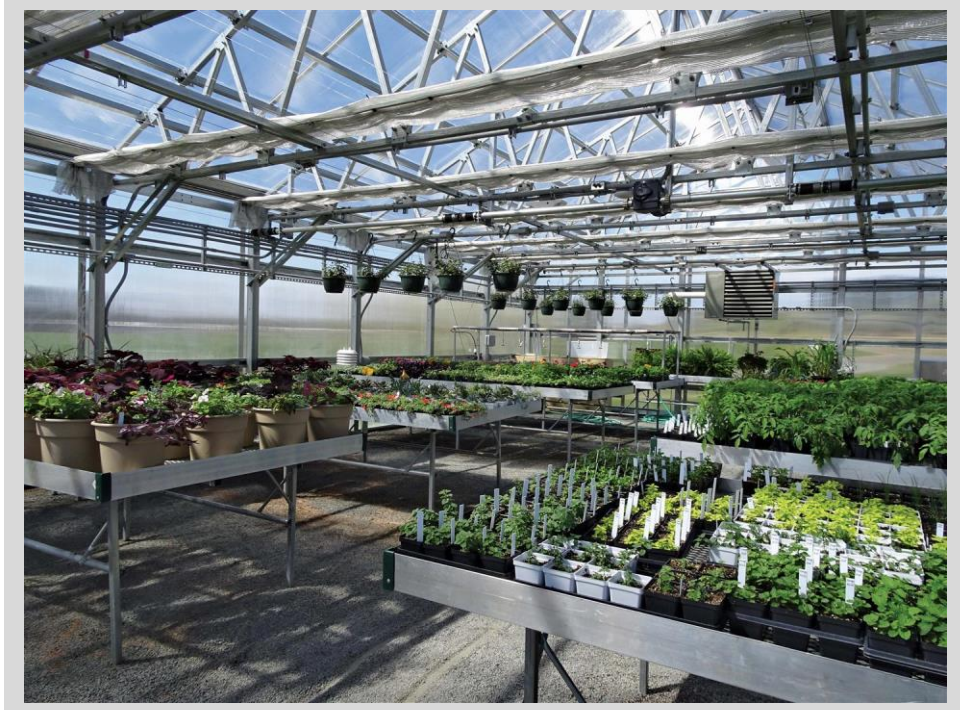



# PROJECTS

